

Project: HangPro 2

LRQA PRJ No: PRJ11100512208

Client: Gripple

Office: Don Road I&I

Client's Order No: P/081536

Order Status: Completed


Inspection Date: 17/06/2024

First: 17/06/2024

Final: 17/06/2024

This certificate is issued to Gripple Ltd to certify that the undersigned surveyor did, at their request attend the premises at The Innovation Centre, Sheffield on and between the above dates for the purpose of examining and witnessing tests on the items listed below. All tests produced satisfactory results.

TEST CONFIGURATION

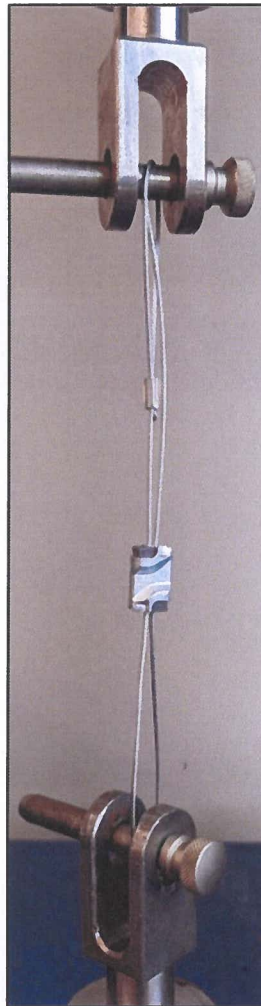

Gripple Model	Safe Working Load (5:1) (Kg)	Max Working Load (Kg)	Results (Kg)	Average (Kg)
HangPro 2	55	275	347.9 343.3 346.4	345.9

LRQA Verification Ltd
 Witnessed Monitored Reviewed

Name: M. Cobb Signature
Date: 17/6/24
Ref. No.:
Office: Birmingham
